intuitive

Agent Dashboard (AI Garage Agent Dashboard)

A single trusted dashboard to track AI agent delivery, blockers, costs, and operational reliability.

WHY

Intuitive's AI Garage is building multiple agents across Azure, AWS, GCP, and local laptops without a central place to monitor delivery progress, spend, or operational uptime. Leadership lacks real-time portfolio visibility without manually interrogating teams, while the Agent Manager must chase updates by hand. Consequently, project blockers and schedule slips go unnoticed until deadlines are compromised.

WHAT WE WILL DELIVER

1. **Agent Governance & Delivery Portal:** Role-based access control enabling contributors to submit progress, an approval workflow for the Agent Manager, audit trails, and automatic escalation for blockers and slipping dates.
2. **FinOps & Automated Health Monitoring:** Programmatic ingestion of usage, model cost tracking, heartbeat health checks, and alerting for agent downtime and cost spikes.

WHAT THE HEAD OF AI GARAGE GETS


- **Portfolio Health Register:** Complete visibility into every active agent's target date, status, assigned owner, and marketplace readiness.
- **Governed Update Workflow:** Contributor self-service submissions that alter status and progress only after review and approval.
- **Early Warning System:** Automated email escalations and slip badges the moment an agent stays blocked for 3+ days or dates slip.
- **FinOps & Anomaly Tracking:** Cost attribution by model and call volume, supported by automated anomaly alerts and budget thresholds.
- **Heartbeat Observability:** Direct machine-to-dashboard health telemetry alerting owners within 15 minutes of an agent outage.

HOW IT FITS TOGETHER


React SPA / Machine Agents → Express API (Auth & Validation) → Review & Rules Engine → Databricks SQL Warehouse → Email Alerts (Azure Communication Services)

intuitive


A single container hosts both the UI and API while relying on standard HTTPS pushes, avoiding direct infrastructure access and eliminating dependencies on corporate IT approvals.

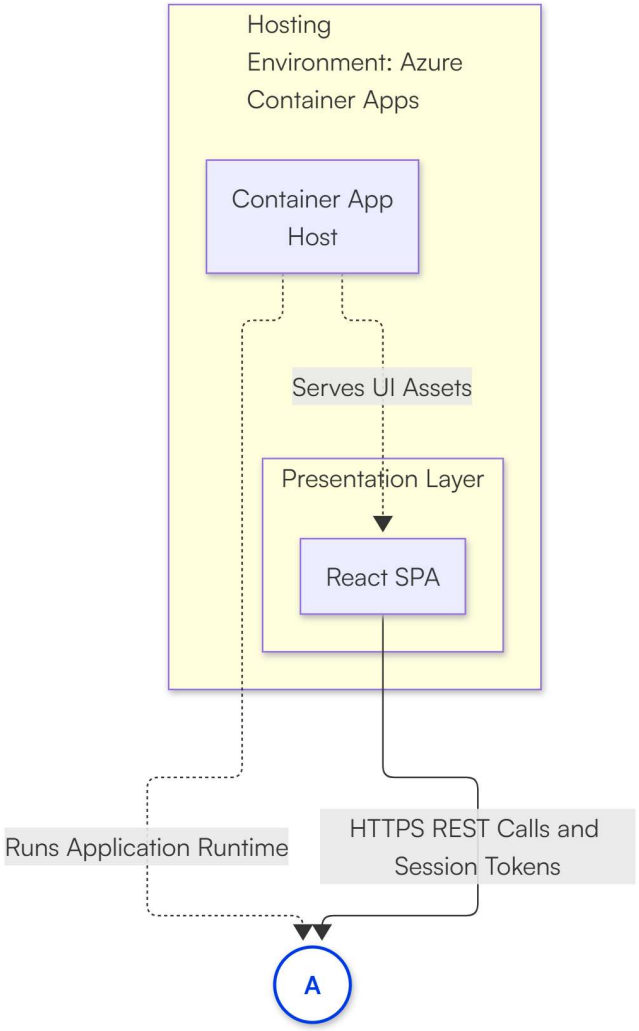


Architecture (part 1 of 5)

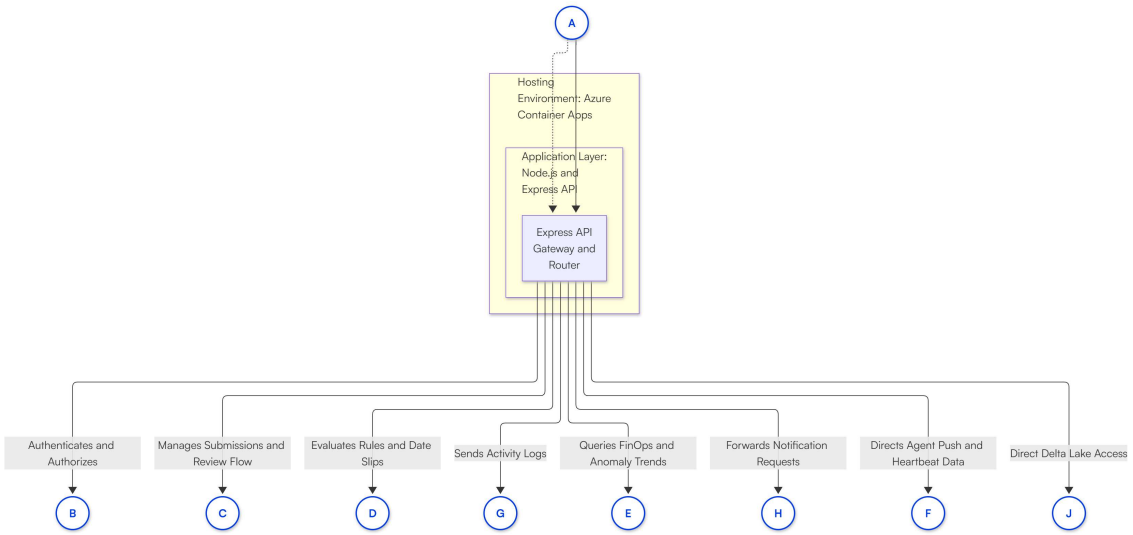

Architecture (part 2 of 5)

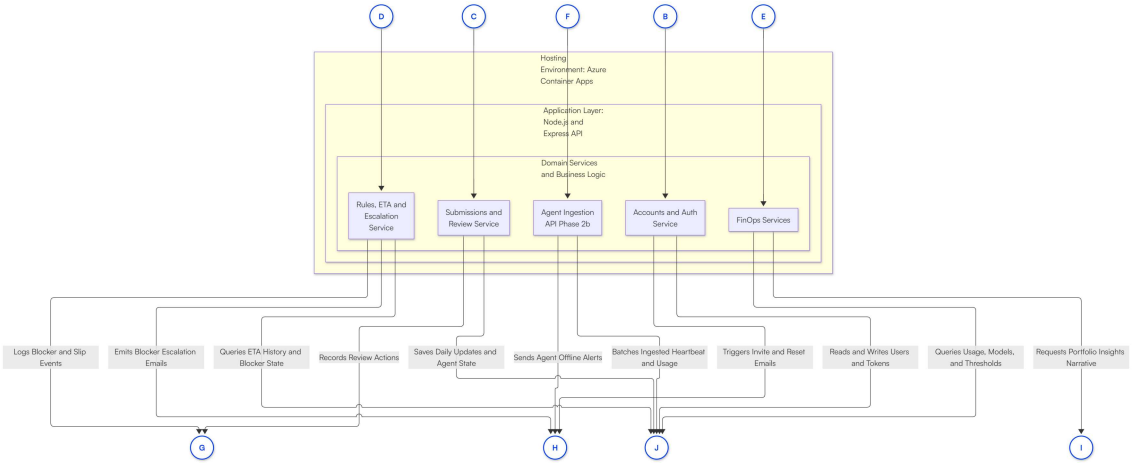


Architecture (part 3 of 5)

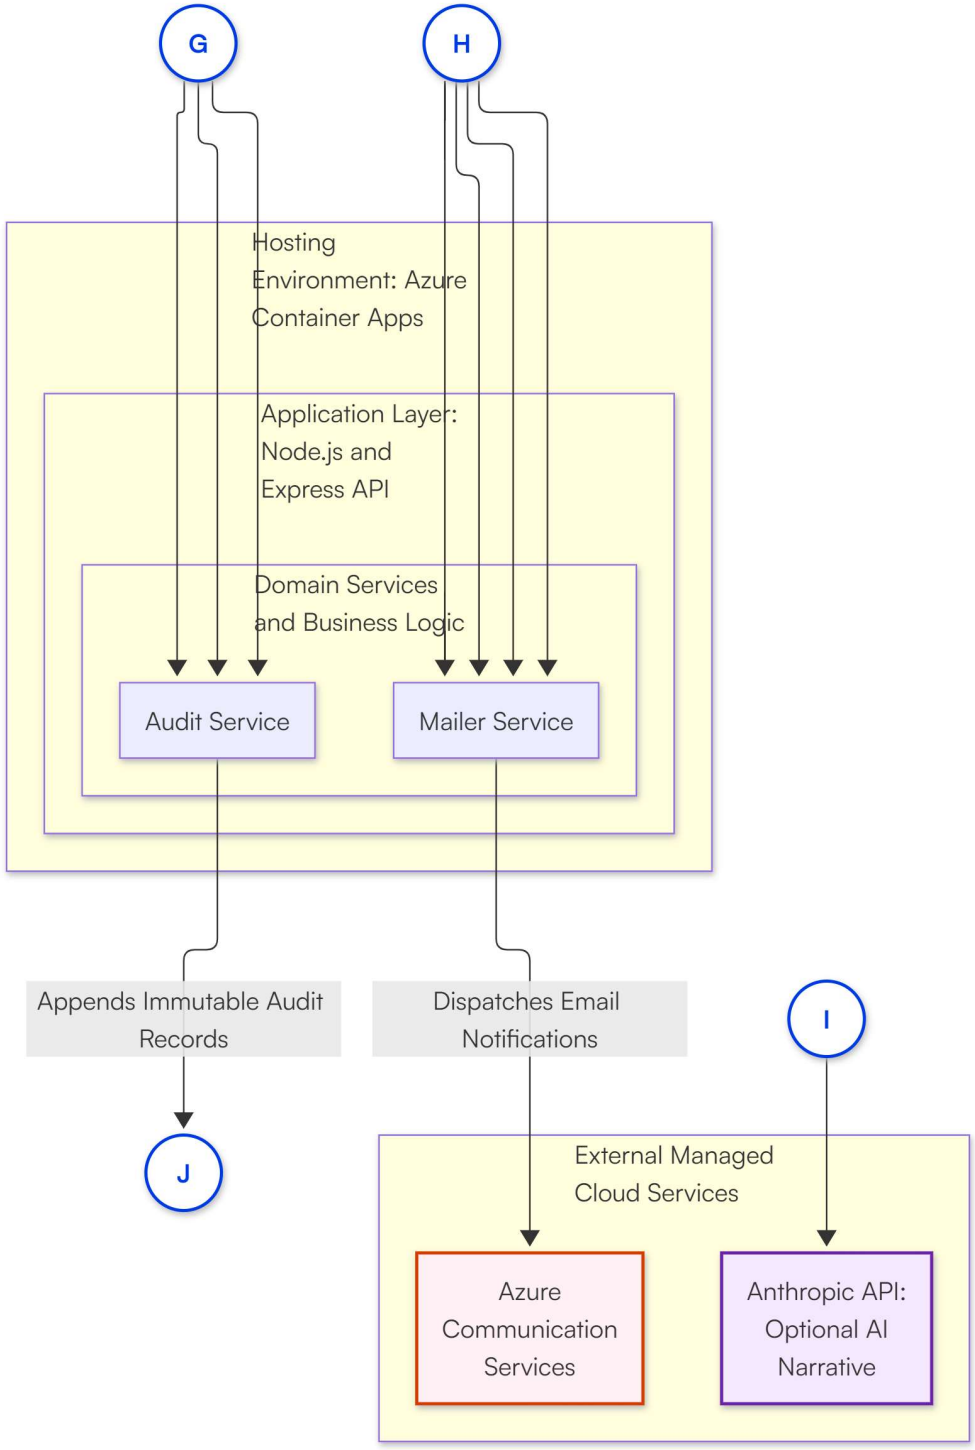

Architecture (part 4 of 5)

intuitive



Architecture (part 5 of 5)

QUESTIONS IT WILL ANSWER

- Which agents are currently blocked, why are they blocked, and who owns unblocking them?
- Which project target dates have slipped, by how many days, and for what reason?
- What is each AI agent costing across platforms, and which models drive high expenditure?
- Which production agents are currently running, and which have stopped sending heartbeats?
- Which active agents have not provided an approved status update in the last 7 days?

WHAT IT DELIBERATELY EXCLUDES

- **Direct database or infrastructure connections:** Agents push summary data over HTTPS to keep internal agent network perimeters fully isolated.
- **Storage of agent prompts and business payloads:** Restricting ingestion to operational metadata protects data privacy and lowers storage footprint.
- **Project management task and sprint tracking:** Focuses exclusively on agent delivery and operational health rather than duplicating Jira or issue trackers.
- **Executive write access:** Enforces view-only permissions for leadership to safeguard reporting integrity and governance.

intuitive

- **Microsoft SSO (Entra ID app registration):** Local invite-based accounts bypass corporate IT access delays to maintain delivery velocity.
- **Active agent control features (start/stop):** Visibility and telemetry must be proven and trusted before introducing remote operational control.

HOW WE WILL DELIVER IT

- **PHASE 1:** Agent tracking, daily updates, FinOps, Azure deployment (Live).
- **PHASE 2a:** Accounts, submit and review, My Agents, audit log, ETA slips, blocker escalation, tests and CI (Built, tested; deploy paused).
- **PHASE 2a deploy:** Migrations 010—013 on live schema, email setup, container rollout, and merge to main.
- **PHASE 2b:** Per-agent API keys, HTTPS push, heartbeat tracking, offline alerts, and integration code snippets.
- **PHASE 3:** Weekly executive summary email, Teams notifications, A2A test tasks, control actions, and Microsoft SSO.

Phases 2a deploy and 2b depend directly on the live Databricks and Azure foundation established in Phase 1.

DECISIONS WE NEED FROM LEADERSHIP

Decision	Owner	Why it matters now
Approve Phase 2a production deployment resumption	Head of AI Garage	Unfreezes paused live rollout, activating personal accounts and governance.
Name designated agent onboarding leads for Phase 2b	Head of AI Garage	Ensures builder teams embed heartbeat and usage push snippets into runtimes.
Confirm success metric target baselines	Head of AI Garage	Establishes enforceable SLA targets for review turnaround and weekly updates.
Appoint secondary reviewers alongside Agent Manager	Head of AI Garage	Prevents Arya Kayastha from becoming an operational bottleneck as agents scale.

intuitive

RISKS WE ARE MANAGING OPENLY

- **A single reviewer creates an approval bottleneck:** Review capability is implemented as a permission rather than a fixed role, enabling team leads to review when volume demands.
- **Migration 013 triggers false-alarm escalation emails on day one:** Agent Managers will be briefed prior to deployment to verify backfilled blocker durations before the first hourly check executes.
- **Azure Communication Services daily sending limits cause dropped alerts:** Rate-limited sending is configured, and personal account invites feature a manual copy-link fallback.
- **Databricks connection resets (ECONNRESET) interrupt CI or writes:** The application includes automated reconnection handling, and extensive integration suites run before each deployment.

THE ASK

Approval to execute the Phase 2a production deployment—applying migrations 010—013 to the live Databricks schema, launching personal authenticated accounts, and merging to main. Following this deployment, leadership will evaluate contributor adoption and SLA baselines before initiating Phase 2b telemetry onboarding.

Full detail in BRD-AGD-001.
